MODERNIZING DIGITAL BANKING OPERATIONS

Final project | corrected, rubric-aligned presentation | 1 November 2026

REVISED SUBMISSION — COMPLETE PROJECT DESIGN

Retail bank modernization across onboarding, transfers, bill payments, lending, security, data and delivery.

All budgets, targets, schedules, scores and test outcomes are illustrative assumptions, not production results.

This submission addresses the partial-credit criteria through explicit named tables and readable diagrams.

01 | EXECUTIVE SUMMARY

Problem statement, insights, recommended actions

- Problem: fragmented digital journeys, manual exceptions and batch-dependent integrations delay customer service.
- Insight: preserve the authoritative core ledger while adding governed APIs, orchestration and immutable audit trails.
- Value: simplify onboarding, payments, transfers, lending status and reconciliation through reusable services.
- Proposed targets: 30% lower onboarding time; 99.95% availability; at least 99.9% posting reconciliation.
- Delivery: baseline and discover, prove with synthetic data, design/build, verify, pilot, hand over.
- Recommended action: approve a 24-week gated plan with security, compliance and recovery sign-offs.

02 | INTRODUCTION

Opportunity, approach and testable hypotheses

- Opportunity: replace channel silos and opaque payment status with secure, accessible self-service journeys.
- Discovery: inventory customer journeys, SLAs, upstream vendors, core banking interfaces and control obligations.
- Method: baseline time, errors and operational support contacts; map target workflows and exception handling.
- H1: reusable KYC and electronic consent decrease median onboarding completion time by at least 30%.
- H2: unique idempotency keys prevent duplicate ledger postings despite API retries.
- Q1: can supported core adapters provide status publication within five seconds for 95% of changes?
- Q2: can RBAC, MFA, encryption and consent logs support control-based audit review?
- Q3: can planned availability (99.95%), RPO (15 min) and RTO (2 h) be evidenced in tests?

03 | BUSINESS OBJECTIVES

Seven independently measurable objectives; targets require baseline confirmation

Area	SMART objective	Evidence / measurement
Efficiency	Reduce median onboarding completion time at least 30%	Funnel and time-study comparison
Scalability	Sustain 3x forecast peak traffic; p95 API <= 500 ms	Load and stress run
Security	100% privileged MFA; no critical unmitigated findings	IAM and security signoff
Modernization	Expose 4 governed journey APIs; automate 80% chosen steps	API inventory and process review
Real-time integration	95% of status changes delivered in <=5 seconds	Event lag telemetry
Data management	>=99.9% reconciliation matching and PII lineage	Daily reconciliation and lineage review
Resilience	Availability >=99.95%, RPO <=15m, RTO <=2h	SLO monitoring and failover drill

04 | PROJECT CHARTER (1/2)

Authority, business case, objectives and scope

Charter field	Substantively defined content
Project title / date	Modernizing Digital Banking Operations | 1 Nov 2026
Description	API-led, regulated transformation of retail customer journeys while retaining core ledger as source of truth.
Sponsor / manager	Chief Digital Officer (sponsor); Program Manager (delivery); Product Owner (requirements).
Objectives	30% faster onboarding; 3x load; 99.95% availability; secure payments and traceable data.
Success criteria	>=99.9% reconciliation; status >=95% within 5s; no critical open security findings; signed pilot UAT.
High-level requirements	Consent + KYC; idempotent transfers; fraud/limit screening; lending decision audit; MFA/RBAC; recovery.
In scope	Onboarding, funds transfers, bill payment, loan applications; identity, fraud, API, audit and reporting.
Out of scope	Core-ledger replacement; new credit policy; trading; card network replacement; branch closure.

04 | PROJECT CHARTER (2/2)

Governance, assumptions, budget and approval

Charter field	Substantively defined content
Stakeholders and roles	Sponsor approves spend; Product owns UX; Core Banking owns adapters; CISO owns security; Privacy/Compliance approves policy; SRE operates; Data Lead reconciles.
Deliverables	Approved charter/BRD, WBS, RTM, use cases, DFD/ERDs, interfaces, PoC, validated tests, release/rollback runbooks.
Assumptions	Supported core APIs available; approved sandbox/cloud tenancy; synthetic PoC data; partner KYC/fraud test endpoints available.
High-level risks	R-01 vendor timeout; R-02 duplicate post; R-03 account takeover; R-04 core outage; R-05 PII exposure; R-06 migration defect.
Milestones	Weeks 1–5 plan; 6–10 design/PoC; 11–17 build; 18–21 verify; 22–24 pilot, handover, closure.
Illustrative budget	Total $1,200,000: delivery labor $690k; cloud/tooling $160k; security/testing $110k; vendors $130k; contingency $110k.
Approval criteria	Steering funding approval; signed architecture, compliance and risk gates; evidence-backed go/no-go before pilot.

05 | STAKEHOLDER REGISTER (1/2)

Required fields: name, role, attitude, interests, impact, influence, preferences, location, success, hours

Stakeholder	Role	Attitude	Interest	Impact	Influence	Comms	Location	Success	Work hours
Executive sponsor	Fund / prioritize	Supportive	Value / ROI	High	High	Biweekly board deck	Chicago HQ / hybrid	Funded gates	Mon–Fri 9–5 CT
Product owner	Journeys / UAT	Supportive	Customer adoption	High	High	Weekly demo	Chicago / hybrid	Signed UAT	Mon–Fri 9–5 CT
CISO / fraud lead	Security gates	Cautious	Fraud / threat	High	High	Design gate / brief	US / remote	No critical findings	Mon–Fri 9–5 CT
Compliance / privacy	Consent / policy	Cautious	PII / adherence	High	High	Gate review / email	Chicago / hybrid	Audit-ready evidence	Mon–Fri 9–5 CT

05 | STAKEHOLDER REGISTER (2/2)

Additional operational and customer stakeholders; representative role groups, not identified persons

Stakeholder	Role	Attitude	Interest	Impact	Influence	Comms	Location	Success	Work hours
Core banking lead	Ledger / adapters	Cautious	Data integrity	High	High	Twice-weekly interface	Chicago / hybrid	0 duplicate posts	Mon–Fri 8–5 CT
Engineering / API lead	Build and CI/CD	Supportive	Release safety	High	High	Daily standup	US / remote	Pipeline gates met	Mon–Fri 9–6 CT
Operations / SRE	Service readiness	Neutral	Case handling	High	Medium	Runbook / weekly	US / hybrid	RTO <=2h	Shift coverage 24/7
Customer pilot panel	Usability tests	Neutral	Simple journeys	Medium	Low	Milestone surveys	Remote / US	Task success >=90%	Scheduled sessions

06 | STAKEHOLDER ENGAGEMENT PLAN

Every stakeholder has current state, desired state and action strategy

Stakeholder name / group	Current state	Desired state	Engagement strategy
Sponsor / steering	Supportive	Leading	Biweekly KPI, RAID and spend review; approve phase gates
Product owner	Supportive	Leading	Weekly prototype and acceptance workshop
CISO / fraud	Neutral	Supportive	Threat-model sessions; challenge fraud rules; sign control gates
Compliance / privacy	Neutral	Supportive	Consent/data mapping reviews; written control approval
Core banking	Resistant	Supportive	Contract review twice weekly; negotiate adapter safeguards
Engineering / API	Supportive	Leading	Daily delivery sync, architecture demos and pipeline metrics
Operations / SRE	Neutral	Supportive	Incident simulations, runbook drills and support training
Pilot customers	Unaware	Supportive	Accessible prototype, guided usability test and follow-up survey


07 | BUSINESS REQUIREMENTS DOCUMENT

Explicit scope, objectives, assumptions, metrics and boundaries

Required BRD section	Definition / acceptance measures
SCOPE	Modernize four retail digital journeys (onboard, transfer, pay, apply for loan) plus shared identity, consent, fraud, data and API observability. Core owns accounts and ledger.
OBJECTIVES	Reduce onboarding time >=30%; support 3x peak; improve status and reconciliation; make recovery and security independently auditable.
ASSUMPTIONS	Bank approves sandbox/cloud; supported core contracts exist; KYC/fraud vendors provide test endpoints; only synthetic PoC data; dedicated control owners participate.
SUCCESS METRICS	Onboarding -30%; >=99.95% uptime; >=99.9% reconciliation; >=95% status within 5s; p95 <=500 ms at planned load; zero open critical controls.
CONSTRAINTS	Approved retention and consent; restricted production changes; vendor lead times; legacy core throughput; procurement and change windows.
NON-GOALS	No replacement of authoritative ledger; no modification of underwriting policy; no live customer PII in the sandbox.

08 | USE CASE DIAGRAM

Actor associations and system boundary; explicit include relationships

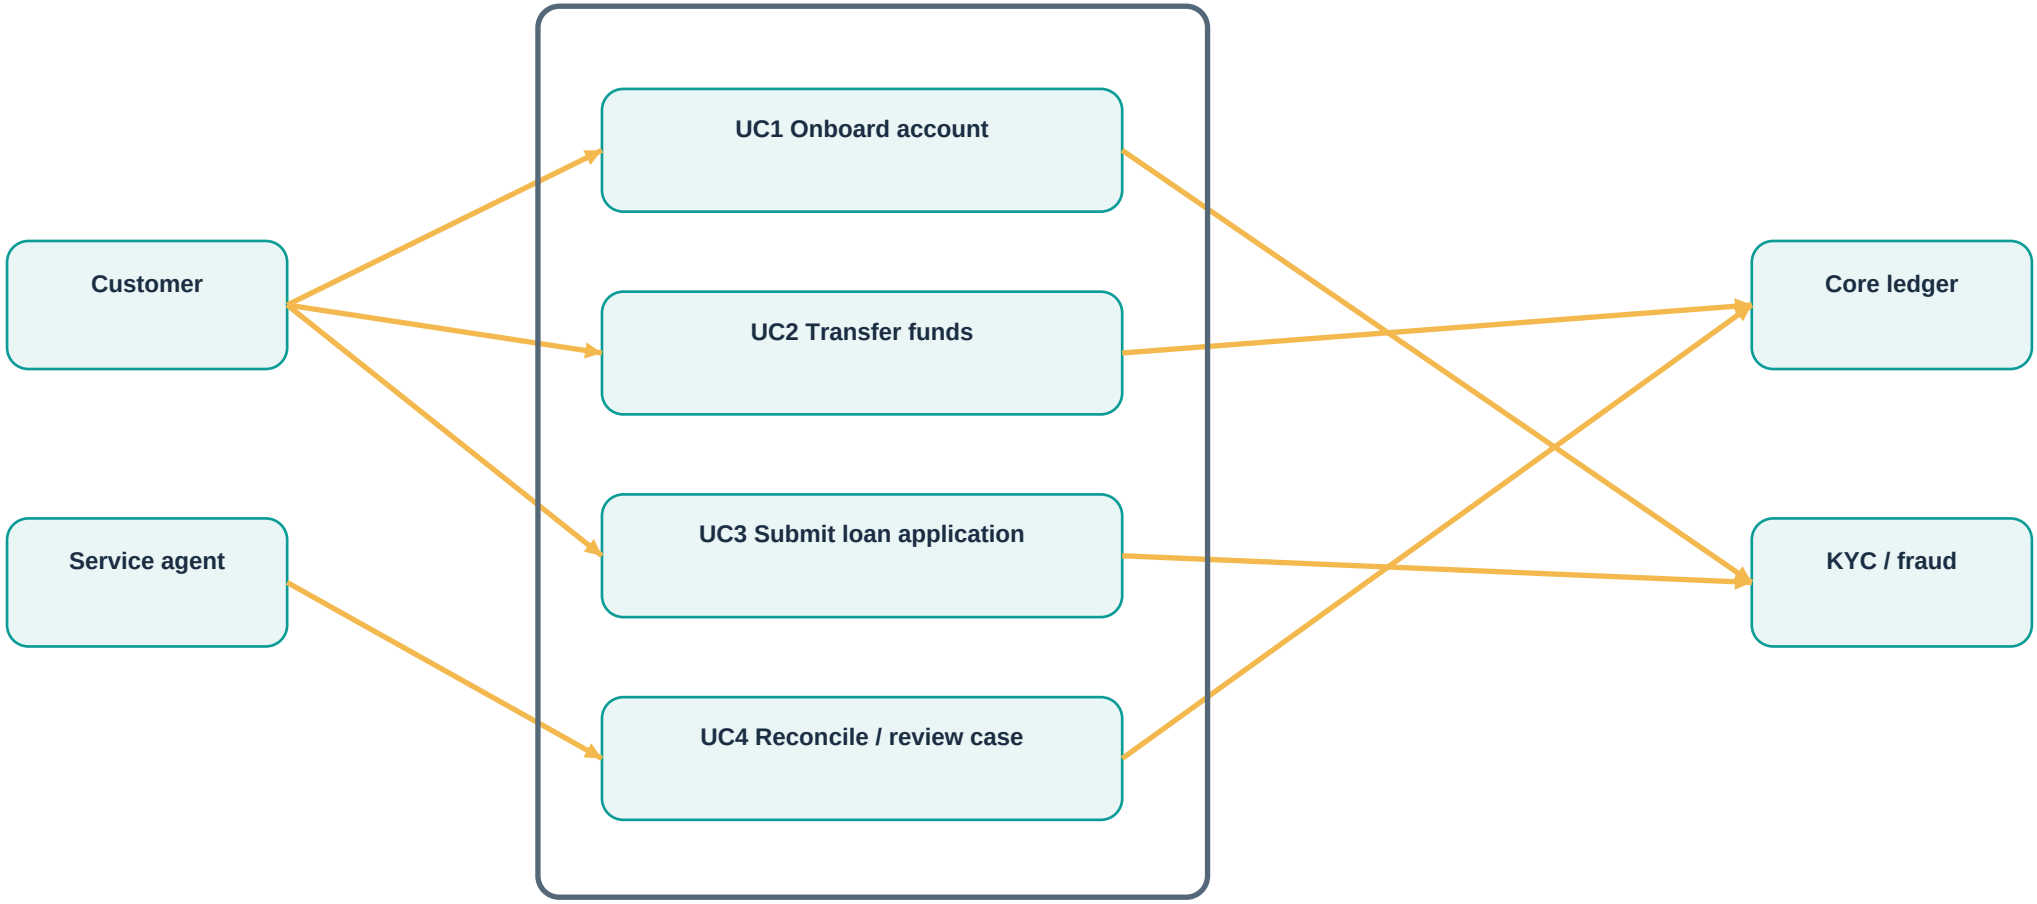

UC1 captures consent and verifies identity; UC2 authorizes once and obtains core confirmation.

UC3 stores loan decision history; UC4 gives a service agent an auditable exception trail.

Mandatory supporting use cases: authenticate (UC1–UC4), screen risk (UC1–UC3), log audit (all).

09 | REQUIREMENTS TRACEABILITY MATRIX

Linkage, ownership, acceptance, testing and risks

ID	Type	Description	Source	Goal	Acceptance	Link	Owner	Priority	Status	Verify	Risk
FR-01	F	Consent + KYC onboarding	Customer/Ops	Time -30%	Consent + KYC logs	NFR-01	PO/IAM	Must	Designed	BDD-01	R01/R05
FR-02	F	Idempotent transfers	Payments	Integrity	Same key=one posting	NFR-03	Payments	Must	Designed	TDD-02	R02/R04
FR-03	F	Lending workflow	Credit Ops	Status	Immutable decision	NFR-01	Lending	Must	Planned	UAT-03	R05/R06
FR-04	F	Fraud/limit gate	Fraud	Prevent loss	Block before post	NFR-01	Fraud	Must	Designed	BDD-04	R03
NFR-01	NF	MFA/RBAC/crypto	CISO	Security	No criticals	FR01/04	Security	Must	Designed	Pen test	R03/R05
NFR-02	NF	Uptime/recovery	SRE	Resilience	99.95%; RPO/RTO	FR-02	SRE	Must	Planned	DR drill	R04
NFR-03	NF	Reconciliation	Finance	Data trust	>=99.9% match	FR-02	Data	Must	Designed	SQL QA	R02/R06


10 | WORK BREAKDOWN STRUCTURE

Numbered phase hierarchy: planning, execution, follow-up and closure

WBS phase	Numbered tasks and subtasks	Completion gate
1.0 PLANNING | W1–5	1.1 Charter + budget; 1.2 baseline KPIs; 1.3 stakeholder register/engagement; 1.4 BRD/RTM; 1.5 initial risk assessment	Sponsor and BRD approvals
2.0 DESIGN + PoC | W6–10	2.1 UX flows; 2.2 DFD/use case/sequence; 2.3 architecture/security; 2.4 ERDs/data mapping; 2.5 PoC plan/test	Architecture/control gate
3.0 BUILD | W11–17	3.1 channel UX; 3.2 adapters/event contracts; 3.3 data staging/mock migration; 3.4 CI/CD + telemetry	Integrated demo
4.0 EXECUTION / VERIFY | W18–21	4.1 BDD/TDD; 4.2 penetration; 4.3 performance; 4.4 reconciliation; 4.5 DR rehearsal and follow-ups	UAT and security approvals
5.0 FOLLOW-UP + CLOSURE | W22–24	5.1 pilot and rollback drill; 5.2 resolve outstanding actions; 5.3 train support; 5.4 handover; 5.5 lessons learned/closure	Operational acceptance

11 | NETWORK DIAGRAM

Dependencies, activities, sequence and durations | 24 weeks



- Planning = A+B, 5 weeks. Execution = C+D+E, 16 weeks. Closure = F, 3 weeks.
- Dependencies: A → B → C → D → E → F (illustrative critical chain, zero planned float).
- Parallel: security design within C; automated tests begin during D; risk and compliance signoff precedes F.

12 | SWOT ANALYSIS

All quadrants populated with current-state observations and future opportunities

SWOT quadrant	Assessment
Strengths	Trusted core ledger; established customer relationships; mature fraud operations; change governance
Weaknesses	Manual exception workflows; latency at legacy interfaces; inconsistent data ownership; fragmented journey tracking
Opportunities	Self-service onboarding; reusable consent; event-driven status; straight-through processing; journey analytics
Threats	Account takeover; third-party availability; changing privacy duties; core outages; migration errors

13 | RISK REGISTER


Six threats: P x I (both on 1–5 scales)

ID	Cause	Event	Impact	Owner	Category	P	I	Score	Trigger	Response
R01	KYC timeout	Onboarding stalls	Dropoff / backlog	KYC Lead	Ops	4	3	12	Timeout >5%/h	Queue / breaker
R02	Retry w/o key	Duplicate posting	Loss / complaints	Payments	Integrity	3	5	15	Duplicate key	Unique key + recon
R03	Session weakness	Account takeover	Fraud / breach	CISO	Security	3	5	15	Challenge spike	Step-up MFA
R04	Core link loss	API outage	Unavailable service	SRE	Availability	4	4	16	p95 >1sec	Queue / failover
R05	Improper roles	Unauthorized PII	Privacy breach	Privacy	Compliance	3	5	15	Access anomaly	Least privilege
R06	Mapping error	Wrong account link	Recon break	Data Lead	Migration	3	4	12	Mismatch >0.1%	Dry runs/quarantine


14 | THREAT AND OPPORTUNITY MATRICES

Verified IDs and scores; low 1–5, moderate 6–11, high 12–25

Threats

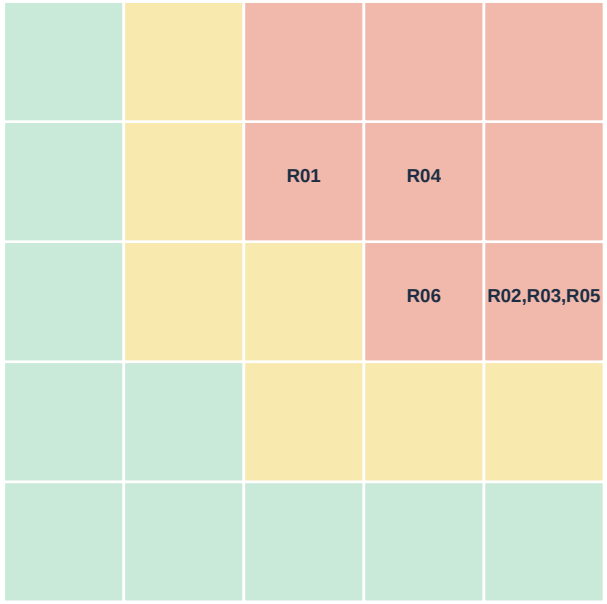


Opportunities

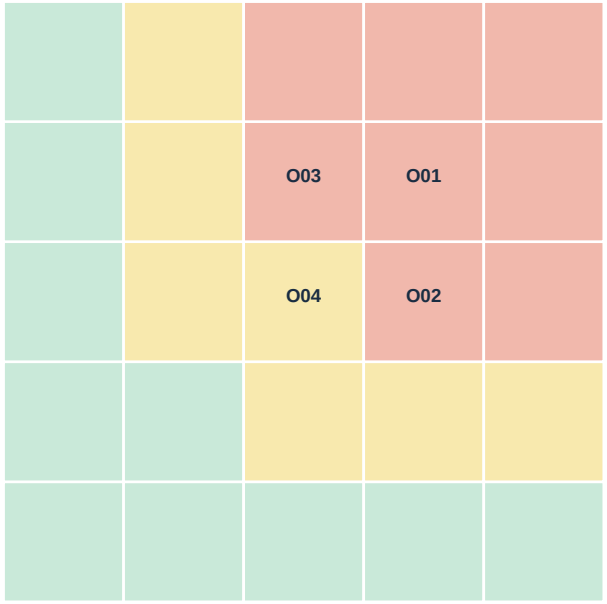

Opportunity register: O01 reusable consent P4 I4 score16; O02 event notices P3 I4 score12; O03 automated regression P4 I3 score12; O04 stuck-journey analytics P3 I3 score9.

15 | CORE BANKING PROCESS FLOW


Explicit branches, decision gates, confirmations and exception handling

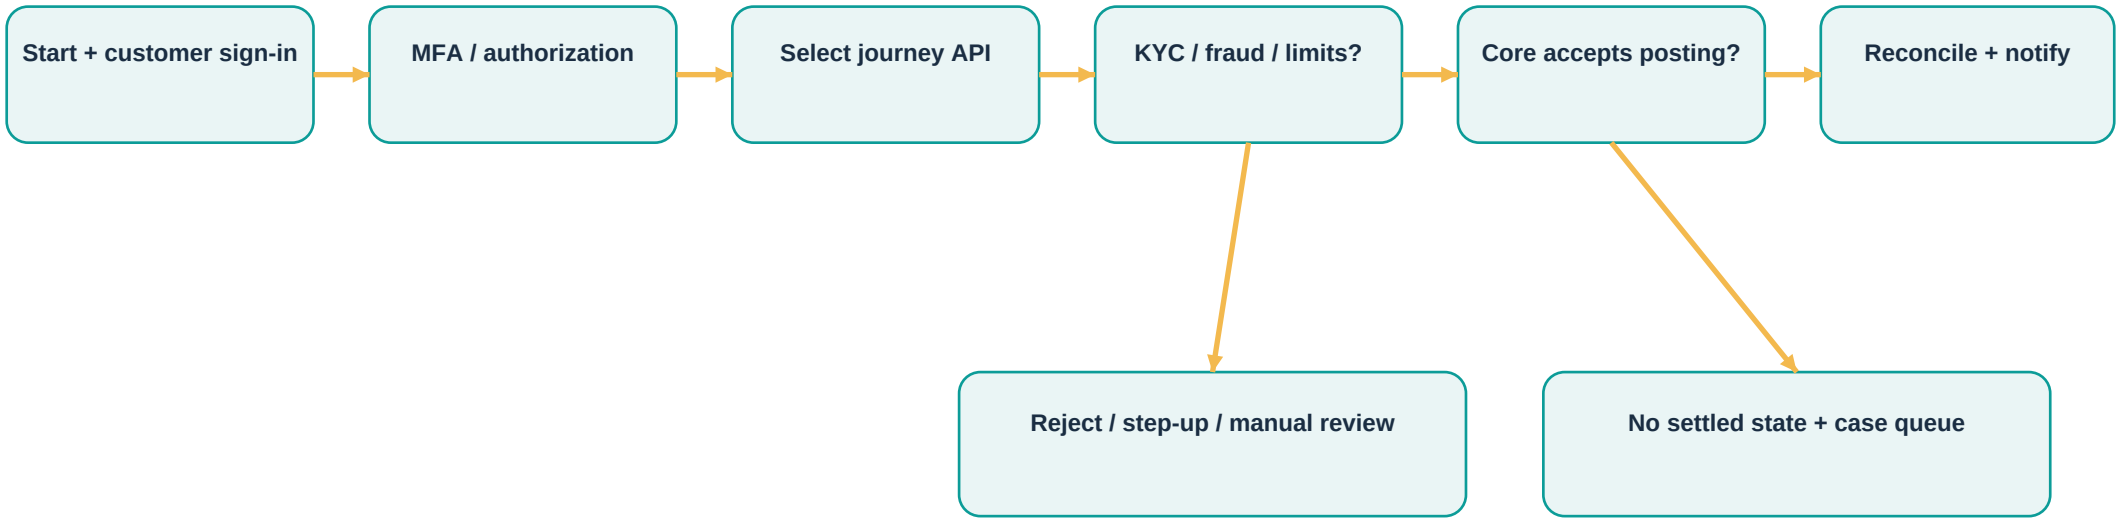

- PASS at control gate → request core adapter posting; FAIL → reject, step-up or investigate.
- PASS at core acknowledgment → reconcile and notify; DECLINE/TIMEOUT → pending/failed, never falsely settled.
- Evidence: correlation ID, consent and fraud decisions, immutable event trace, core confirmation and reconciler case.

16 | SYSTEM DESIGN: DFD LEVEL 0

Context model: external entities and controlled digital banking platform

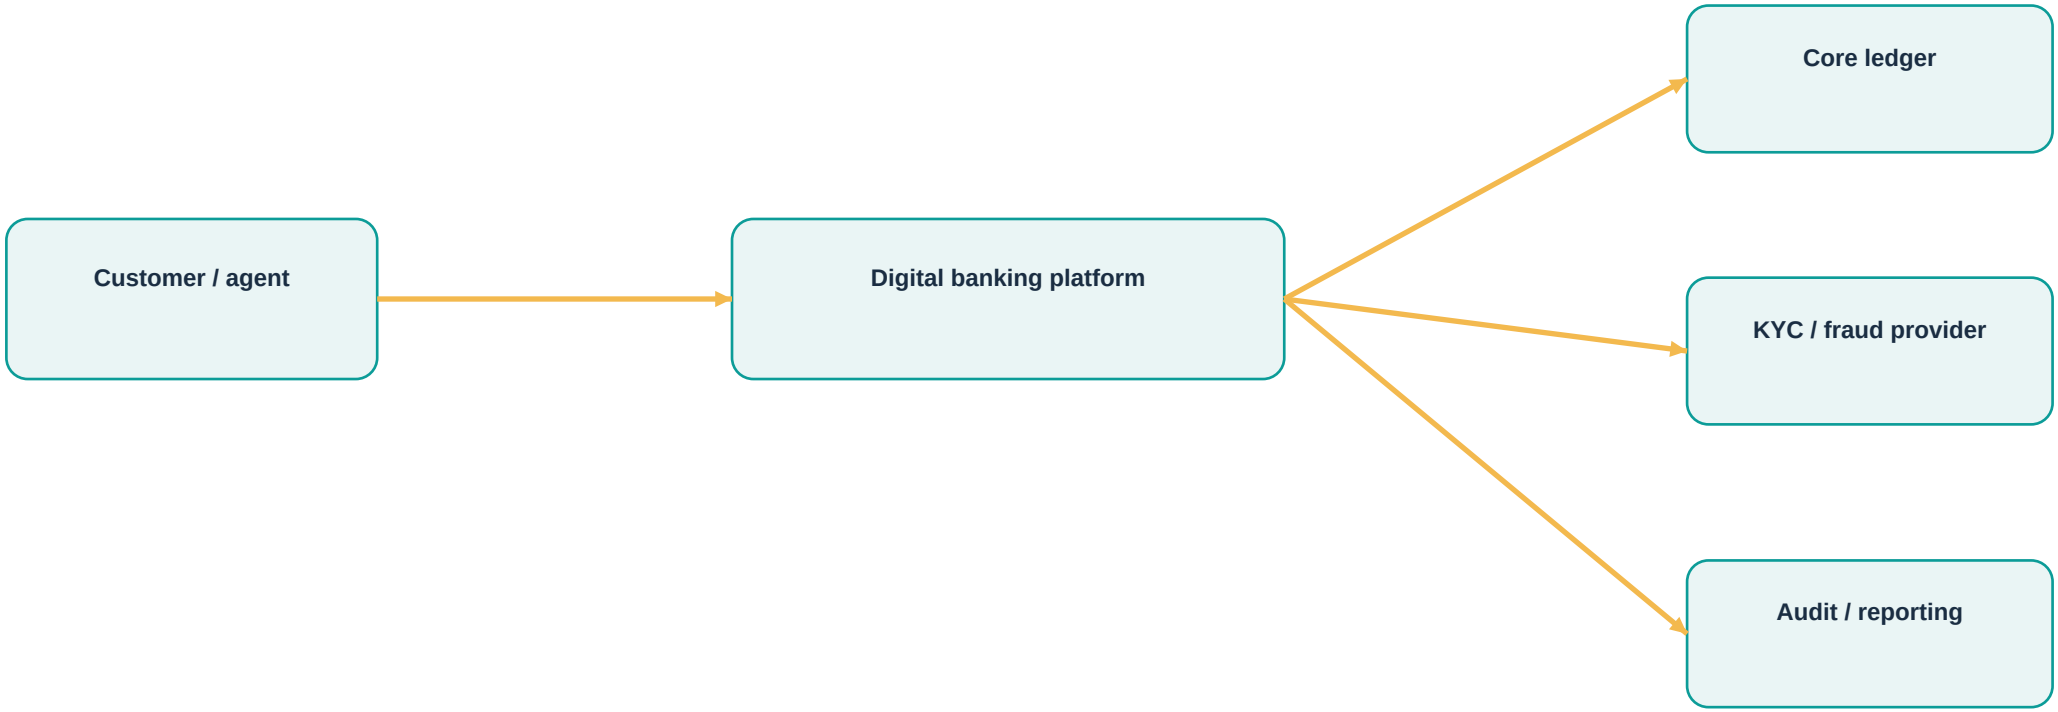


Flows: journey request / confirmation; authorized posting / ledger response; verification / fraud decision;

auditable status, consent, reconciliation and service events. Data-classification boundary: PII encrypted in transit/at rest.

16 | SYSTEM DESIGN: DFD LEVEL 1

Decomposition into separate data stores and functions

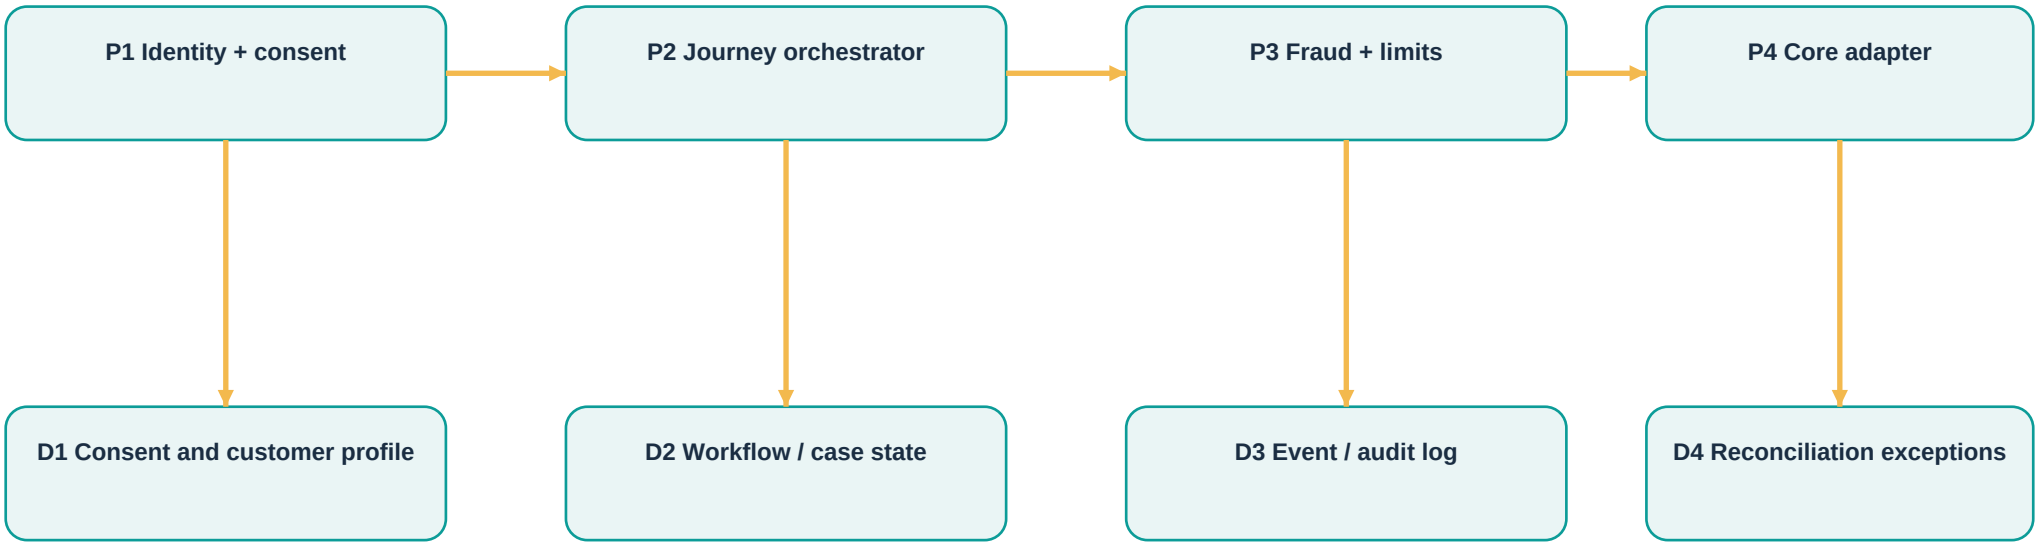


P1 authenticates and records consent; P2 applies idempotency and state machine; P3 evaluates risk; P4 writes via approved ledger contracts.

Persistent stores: D1 profile/consent, D2 cases, D3 append-only events, D4 finance exceptions. No channel owns ledger balances.

16 | SYSTEM DESIGN: SEQUENCE DIAGRAM

Transfer use case: time increases downward

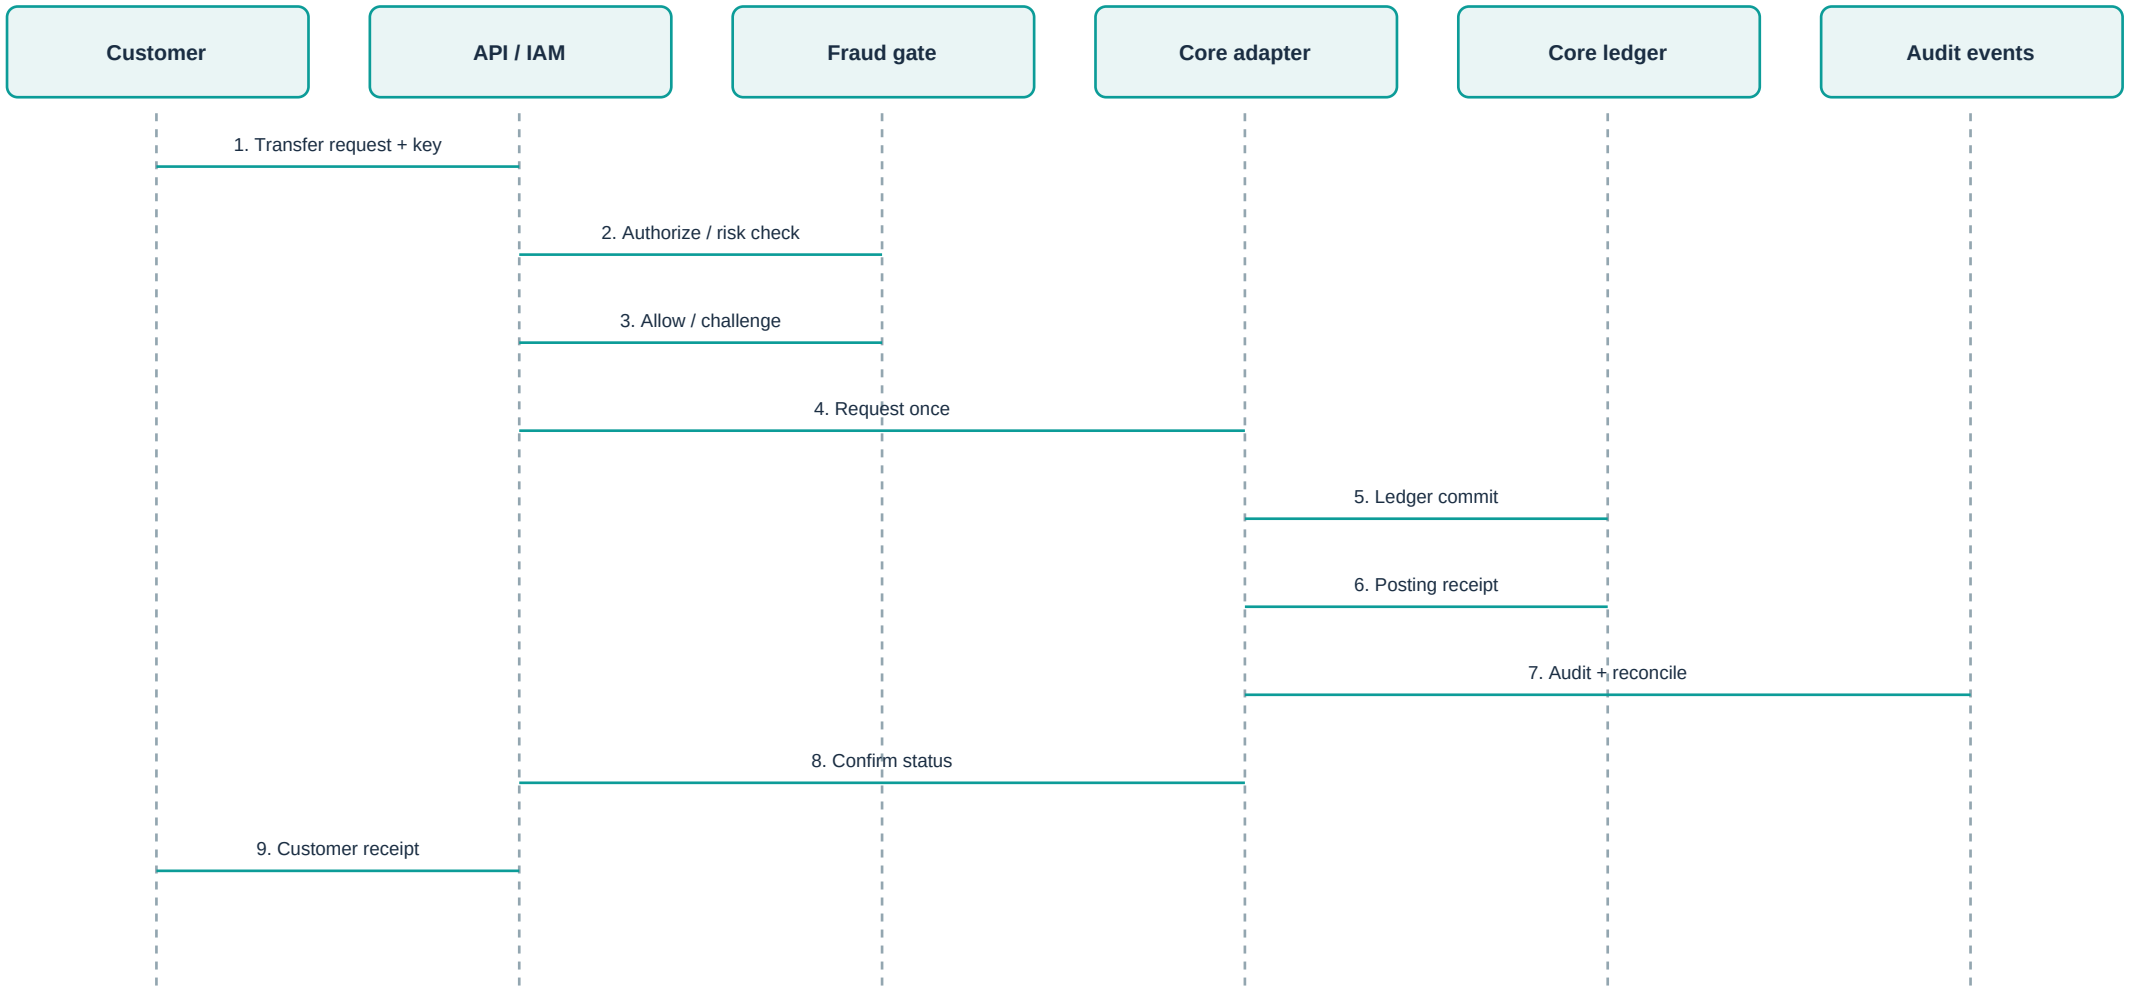

Duplicate request key: adapter reuses prior result; rejection/timeout: emit pending/failed, open case, do not mark settled.


16 | TECHNOLOGY STACK + SYSTEM ARCHITECTURE

Illustrative vendor-neutral pattern, cloud and security zones

Architecture tier	Recommended components / responsibility
Channel	Accessible web/mobile UI, session management, step-up authentication
Edge + API	WAF, throttling, API gateway, OAuth2/OIDC, schema validation and request correlation
Domain services	Stateless onboarding, payment, transfer and lending services; queue/event bus; workflow engine
Core integration	Private adapter layer, idempotency store, timeout/retry budget, ledger acknowledgments
Data	Encrypted relational operational stores, append-only audit, reconciler and curated analytics/lineage
Infrastructure	Private cloud network zones, container runtime, secret vault, managed databases, IaC
Security + SRE	IAM MFA/RBAC, SIEM, vulnerability scans, tracing, alerting, backups and DR test

16 | CLOUD TOPOLOGY + SECURITY ARCHITECTURE

Data flow, isolation and defense in depth

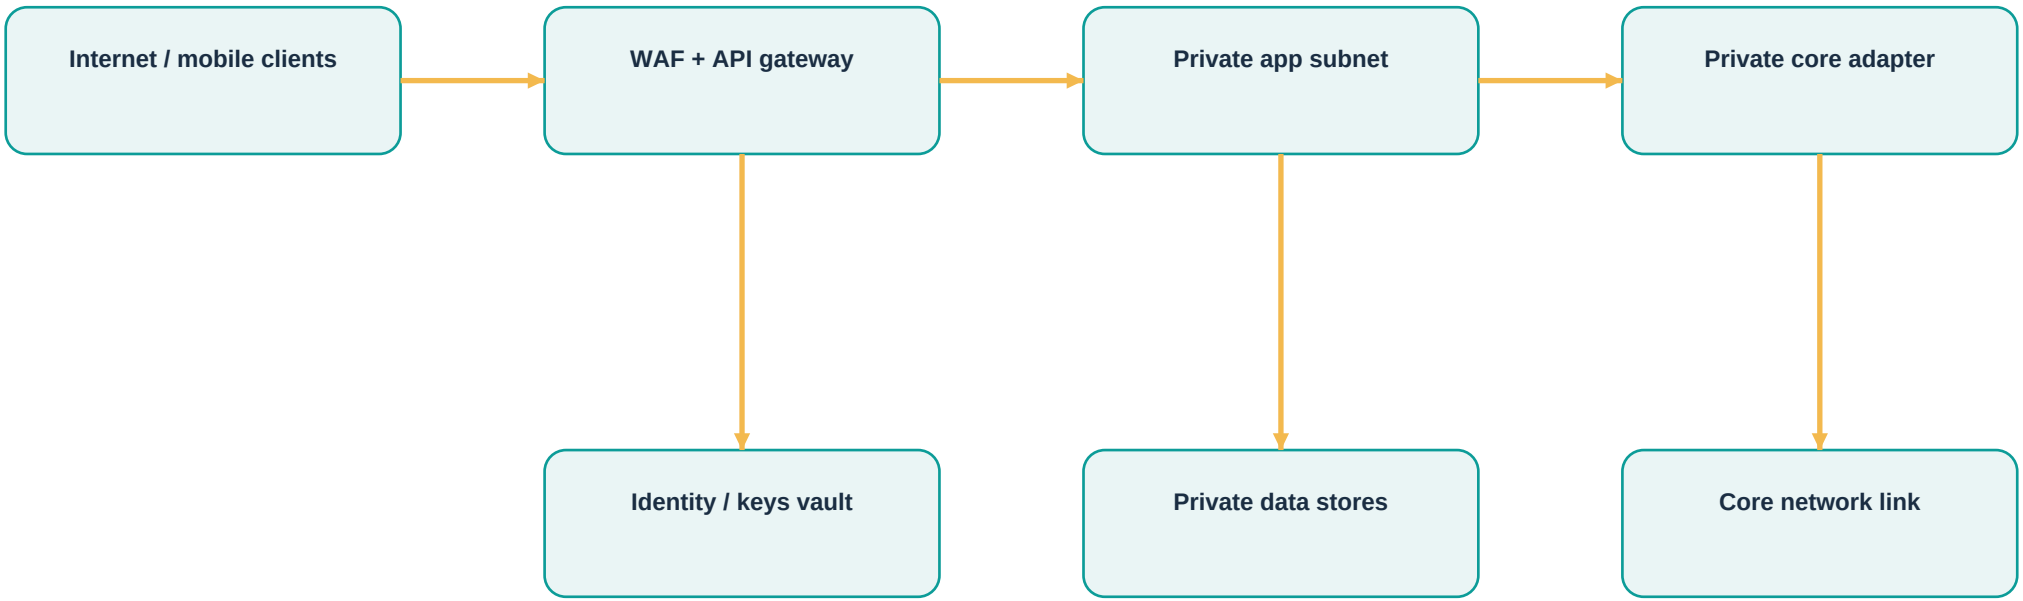

Controls: TLS/mTLS, private endpoints, least privilege, MFA, managed secrets, network segmentation, encryption at rest.

Telemetry → centralized SIEM; CI/CD service identity → signed images/approval gates; separate production from synthetic sandbox.

Core posting requires authenticated service identity; ledger responses are authoritative; immutable audit events support investigations.

17 | PROOF OF CONCEPT (1/2)

Objective, scope, setup, tools and test cases — synthetic data only

PoC item	Proposed procedure / design
Objective	Verify onboarding controls, idempotent transfer and event-status latency before production integration.
Scope	Synthetic customer registration; mocked KYC/fraud; transfer endpoint with duplicate-key replay; reconciliation and alert sample.
Setup	Isolated sandbox, seeded accounts and consent records, test event bus, simulated core ledger, anonymized log output.
Tools	API client, unit/integration tests, SQL assertions, load tool, container registry, telemetry dashboard.
T1 onboarding	Given valid consent + mock KYC pass, account creation request records approval and a traceable core receipt.
T2 duplicate	Given the same transfer key twice, exactly one accepted posting exists; both calls return consistent status.
T3 fraud block	Given a high-risk transfer, the ledger is not called; challenge event and case appear.
T4 lag/recovery	Verify event timestamp delta for <=5s target; simulate failure/replay without duplicates.


17 | PROOF OF CONCEPT (2/2)

Limitations, recommendations and success evidence plan

Table category	Content / recommendation
Limitations	No production connectivity or real customer data; mocked external responses do not reproduce vendor variability.
Limitations	Sandbox latency and uptime do not establish SLA compliance; security claims require independent validation.
Acceptance checks	100% critical consent/audit traceability in scenarios; zero duplicate mock postings; no bypass of fraud challenge.
Evidence artifacts	JUnit output, seeded fixtures, API request/response trace, mock ledger rows, event lag chart, defects register.
Recommendation 1	Complete vendor/core interface contract reviews and security test before controlled integrated test.
Recommendation 2	Evaluate fallback queues, dead-letter handling, status reconciliation and backup restore in failure injection.
Recommendation 3	Approve pilot only after UAT, security/privacy, finance reconciliation and rollback evidence are signed.
Results status	Proposed test design only. No execution metrics or successful live PoC are claimed in this submission.

18 | CONCEPTUAL ENTITY RELATIONSHIP DIAGRAM

Business entities and cardinalities — illustrative financial data model

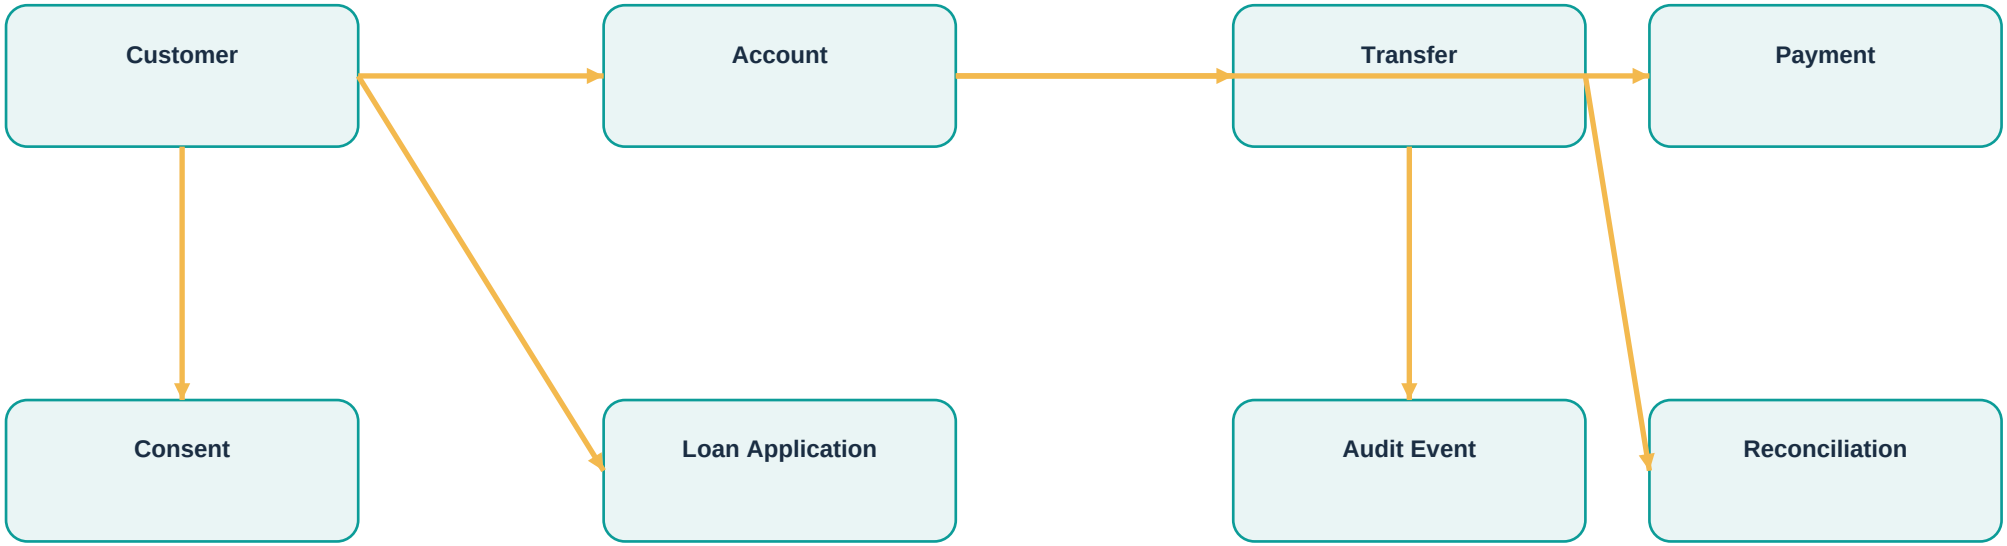

Customer 1:N Account, Consent, LoanApplication; Account 1:N Transfer (source/destination roles) and Payment.

Transfer 1:N AuditEvent, 0..N ReconciliationException. All entity IDs are synthetic and immutable identifiers.

18 | LOGICAL ERD AND NORMALIZATION

Primary keys, foreign keys, relationships, 3NF decisions

Logical entity	Primary key	Selected columns / FK	Normalization / relationship
Customer	customer_id PK	customer_ref UNIQUE; created_at	No repeated contact groups
Account	account_id PK	customer_id FK; core_ref UNIQUE; status	FK Customer; no ledger balance copy
Consent	consent_id PK	customer_id FK; version; accepted_at	Consent history normalized
Transfer	transfer_id PK	source_account_id FK; dest_account_id FK; idempotency_key UNIQUE; state	Both FKs Account; unique key prevents replay
Payment	payment_id PK	account_id FK; payee_id FK; amount; state	Payee stored in separate entity
LoanApplication	application_id PK	customer_id FK; decision_code; decision_at	Status transitions in own history table
AuditEvent	event_id PK	aggregate_type; aggregate_id; occurred_at; event_type	Append only, no user-derived repeats
ReconException	exception_id PK	transfer_id FK; reason; owner_id; state	No duplicated transfer details

18 | DATA DICTIONARY

Data types, constraints, sensitive classification, and stewardship

Field	Type	Constraint / rule	Classification	Owner
customer_id	UUID	PK / not null	Internal	Data steward
customer_ref	VARCHAR(64)	UNIQUE / not null	Confidential	Identity
account_id	UUID	PK / not null	Internal	Core integration
core_ref	VARCHAR(64)	UNIQUE / not null	Confidential	Core team
consent_version	VARCHAR(20)	Not null	Restricted	Privacy
idempotency_key	VARCHAR(128)	UNIQUE / not null	Internal	Payments
amount_minor	BIGINT	Nonnegative	Confidential	Payments
transfer_status	VARCHAR(20)	Enum requested/pending/posted/failed	Internal	Payments
occurred_at	TIMESTAMP TZ	Not null / UTC	Internal	SRE
recon_reason	VARCHAR(100)	Controlled vocabulary	Confidential	Finance


18 | MIGRATION STRATEGY + NORMALIZATION KEYS

Mapping, reconciliation, cutover and rollback with gated data controls

Step / artifact	Detailed control
1 Inventory / classify	Legacy data inventory, PII classification, owners, approved data retention; baseline quality.
2 Map / normalize	Legacy customer/account IDs → UUID keys; reference reconciliation; 1NF atomic fields, 2NF full-key dependency, 3NF no non-key transitive dependency.
3 Profile / cleanse	Detect duplicate customers, inconsistent status, missing consent; quarantine exceptions; document decisions.
4 Synthetic dry runs	Seed masked/synthetic snapshots, validate counts, referential integrity, transformation logs and checksum evidence.
5 Dual-read validation	Compare authoritative core refs and selected read models; daily 99.9% reconciliation match threshold.
6 Cutover gates	Privacy/security signoff, backup restore evidence, freeze plan, downstream notifications and execution owner.
7 Rollback	Disable new read model, route requests back to existing adapter, restore approved snapshot where permitted; preserve authoritative ledger.
Key tables	Customer(customer_id PK); Account(account_id PK, customer_id FK); Transfer(transfer_id PK, account_id FK); Consent(consent_id PK, customer_id FK).

19 | CI WORKFLOW + CD PIPELINE

Source-to-release gates, approvals and automated rollback

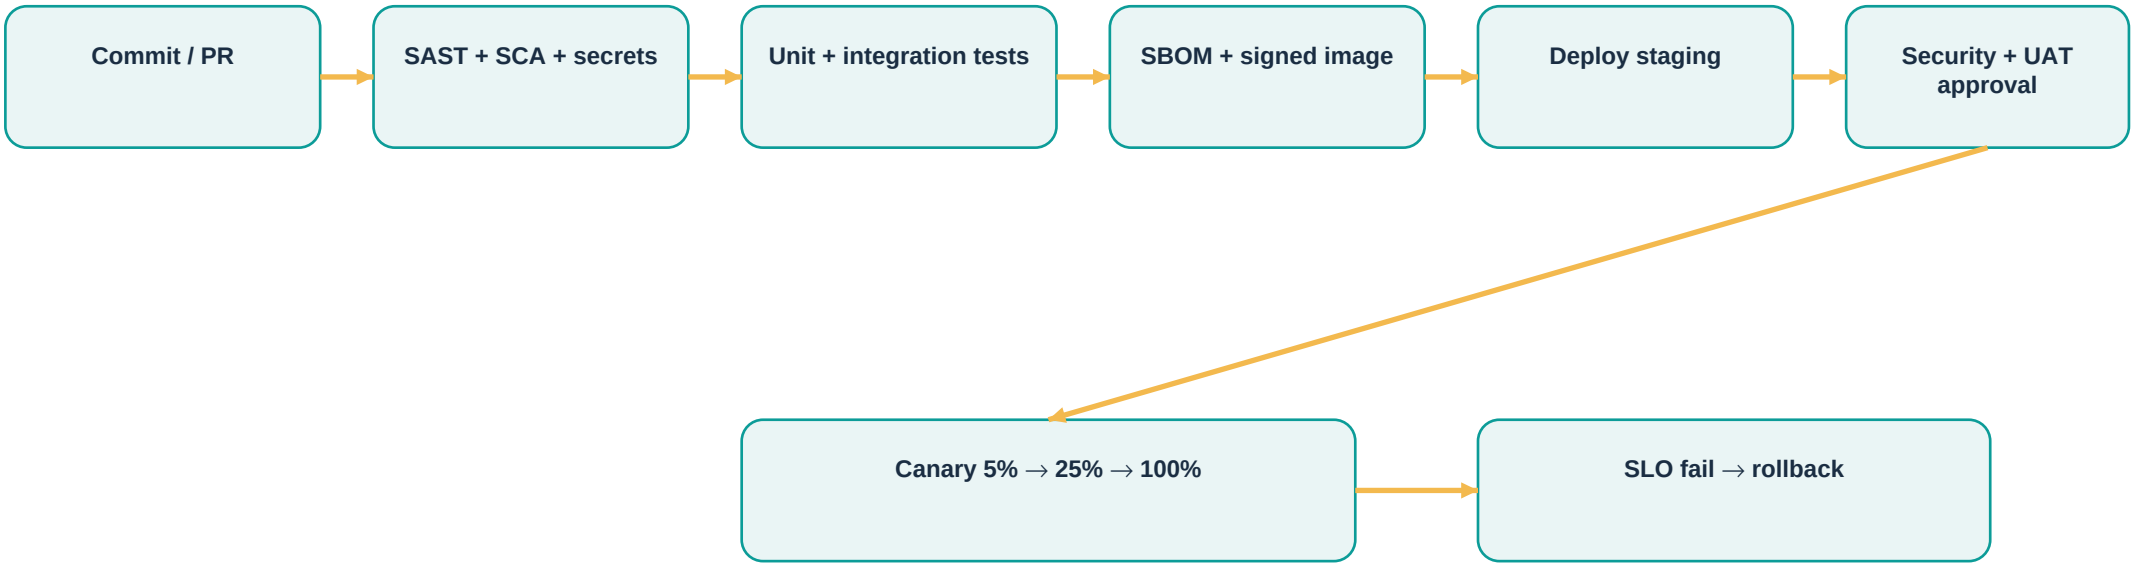

CI: protected branch + reviews, threat-sensitive tests, provenance, vulnerability policy and artifact signing.

CD: IaC plan review, environment-specific secret references, canary traffic and go/no-go based on error, latency, fraud and recon metrics.

Rollback: freeze rollout; restore prior signed image and routing; validate ledger consistency before resuming.

19 | CONFIGURATION GUIDES AND CLOUD COMPONENTS

Required implementation settings; proposals require security review

Configuration area	Configuration guidance
IAM	OIDC federation, short-lived service identities, privileged phishing-resistant MFA, RBAC and quarterly access review.
Network	Separate public edge from private app/data; WAF; restricted egress; mTLS to core; deny direct DB public access.
API / events	Versioned OpenAPI contracts, schema validation, idempotency TTL, retry with jitter, DLQ and correlation IDs.
Secrets / encryption	Managed vault, rotation, envelope encryption, database TDE, approved KMS policies.
CI/CD	Signed container policy, SAST/SCA threshold, PR approval, IaC drift detection and deploy identity scope.
Cloud components	WAF, API gateway, private container cluster, queue/event broker, managed RDBMS, vault, object backups, SIEM.
Operations	SLO dashboards, structured logs without raw PII, runbook links and monthly change evidence export.

19 | BACKUP / RECOVERY AND MONITORING

Evidence-oriented operational playbook, alerts and ownership

Control	Required detail / evidence
Recovery objectives	RPO <=15 minutes; RTO <=2 hours as proposed acceptance targets; tested and recorded during DR exercise.
Backup policy	Encrypted incremental backups every 15m or supported log shipping; daily full snapshots; cross-region copies with tested retention.
Restore rehearsal	Restore to isolated recovery environment, compare row counts/checksums, validate access policies and service replay.
Failure scenarios	Loss of core link, consumer backlog, regional app failure, corrupt mapping, credential compromise; no duplicate core posts.
SLIs / dashboards	Availability, p95 latency <=500ms, error rate, event lag <=5s for 95%, queue depth, reconciliation >=99.9%, fraud challenge.
Alerts / response	Critical unauthorized access → SOC immediately; SLO breach → SRE on-call; finance mismatch >0.1% → data/finance incident.
Cadence / owners	Daily service review (SRE), daily finance reconciliation, weekly release metrics, quarterly failover exercise.
Pilot go/no-go	CISO + privacy, product/UAT, core/finance and SRE sign operational evidence; rollback validated.

20 | VERIFICATION AND SUPPORTING MATERIAL

Acceptance, traceability and recommended evidence package

Evidence category	Artifacts / verification
Functional	BDD-01 consent/onboarding; TDD-02 duplicate key; UAT-03 lending; BDD-04 fraudulent payment rejection.
Non-functional	Load 3x peak / p95 <=500ms; security scan / no criticals; recovery drill / RPO and RTO; ledger reconciliation.
Audit	Versioned BRD/RTM, approval log, consent samples, security risk decisions, migration mapping and exceptions.
Process / design	WBS + network dependency diagram, context and L1 DFD, use cases, sequence, cloud/security diagram, conceptual/logical ERDs.
PoC	Synthetic dataset definition, setup/tool inventory, test scripts, limitations, expected results and defects.
Operations	CI/CD gate logs, signed artifacts, rollout/rollback playbook, SLO dashboard export, recovery rehearsal signoff.

21 | REFERENCES, ASSUMPTIONS AND SIGN-OFF

Proposed design only — this artifact does not represent production implementation

- Primary basis: submitted Modernizing Digital Banking Operations capstone and reviewer rubric feedback (30 October 2026).
- Frameworks consulted conceptually: NIST Cybersecurity Framework 2.0; OWASP ASVS; standard relational normalization/ERD practice.
- Illustrative planning assumptions: 24 weeks; $1.2M budget; synthetic PoC; bank/cloud/vendor approvals not verified.
- All success thresholds are prospective acceptance criteria; passing actual tests requires logs, measurements and authorized reviewer signoff.
- Required signoffs before a real pilot: sponsor, product owner, CISO/fraud, privacy/compliance, core banking, data/finance and SRE.
- Submission cross-check: executive summary, introduction, objectives, complete charter/register/engagement, BRD, use cases, RTM, WBS, network, SWOT, threat/opportunity registers/matrices, process, design, PoC, data and CI/CD.
